



UNNATHI PROJECT PROGRESS UPDATE

In association with:

Tezaswi Garu & Family | Siri Foundation &
Team | Asha for Education | Spoorthi NGO



“With blessings and hope, we lay the foundation for a brighter future.”



www.srujanavani.org

email: info@srujanavani.org

Statutory Approvals

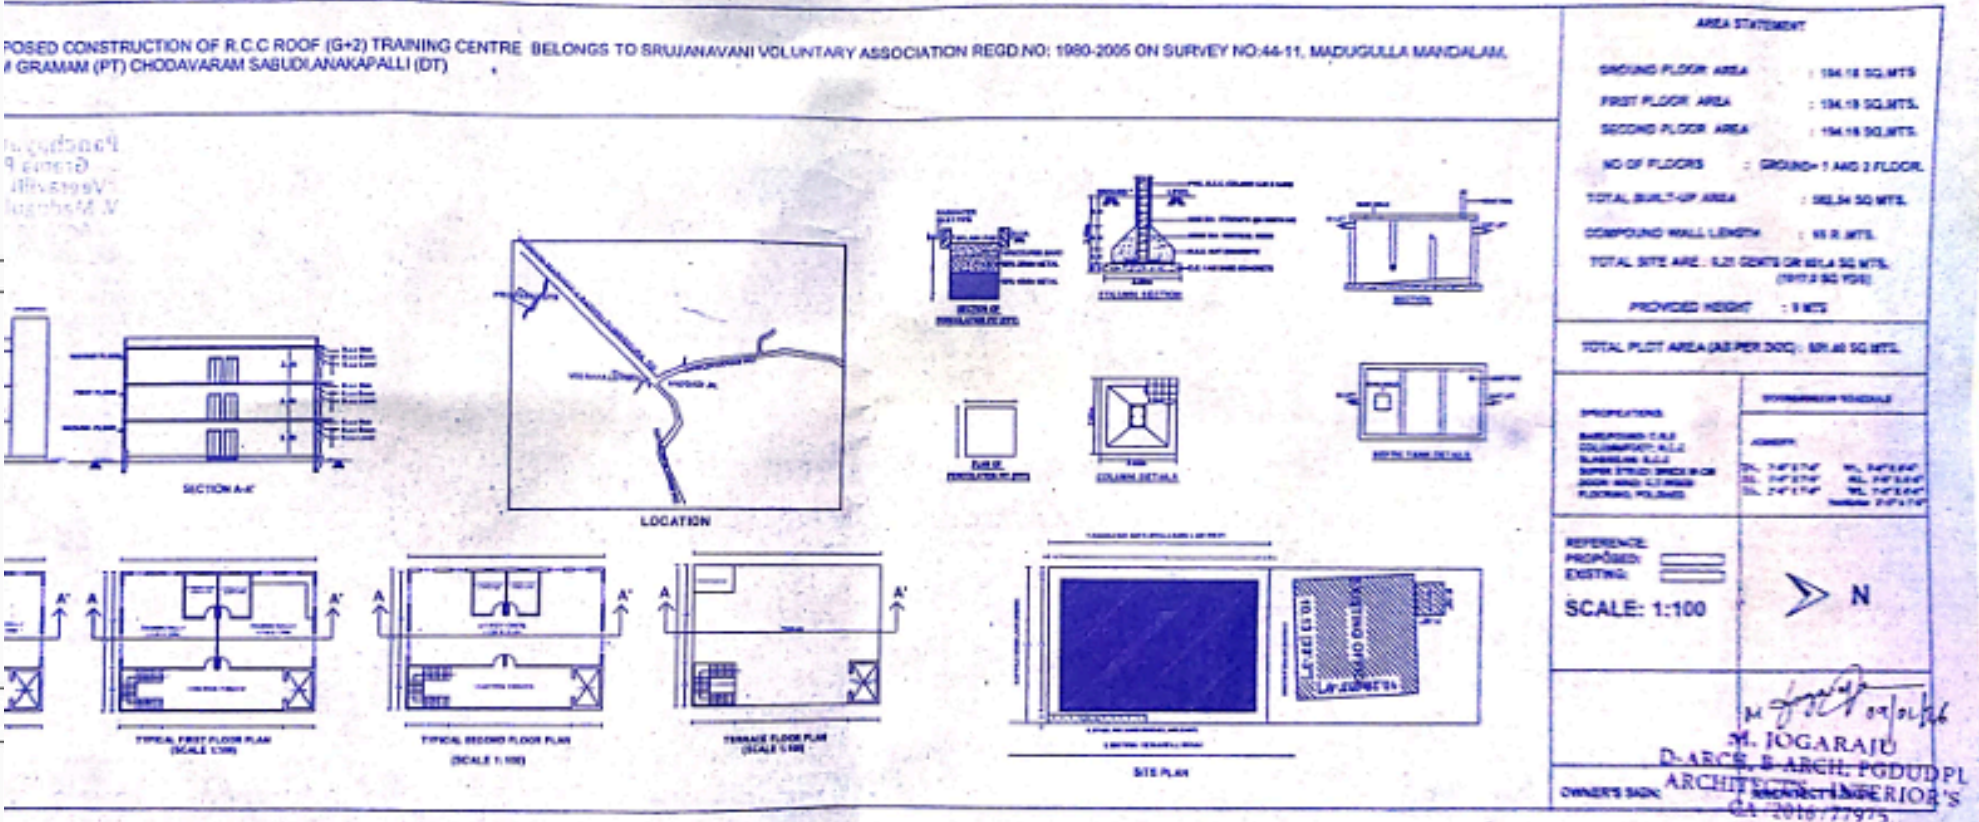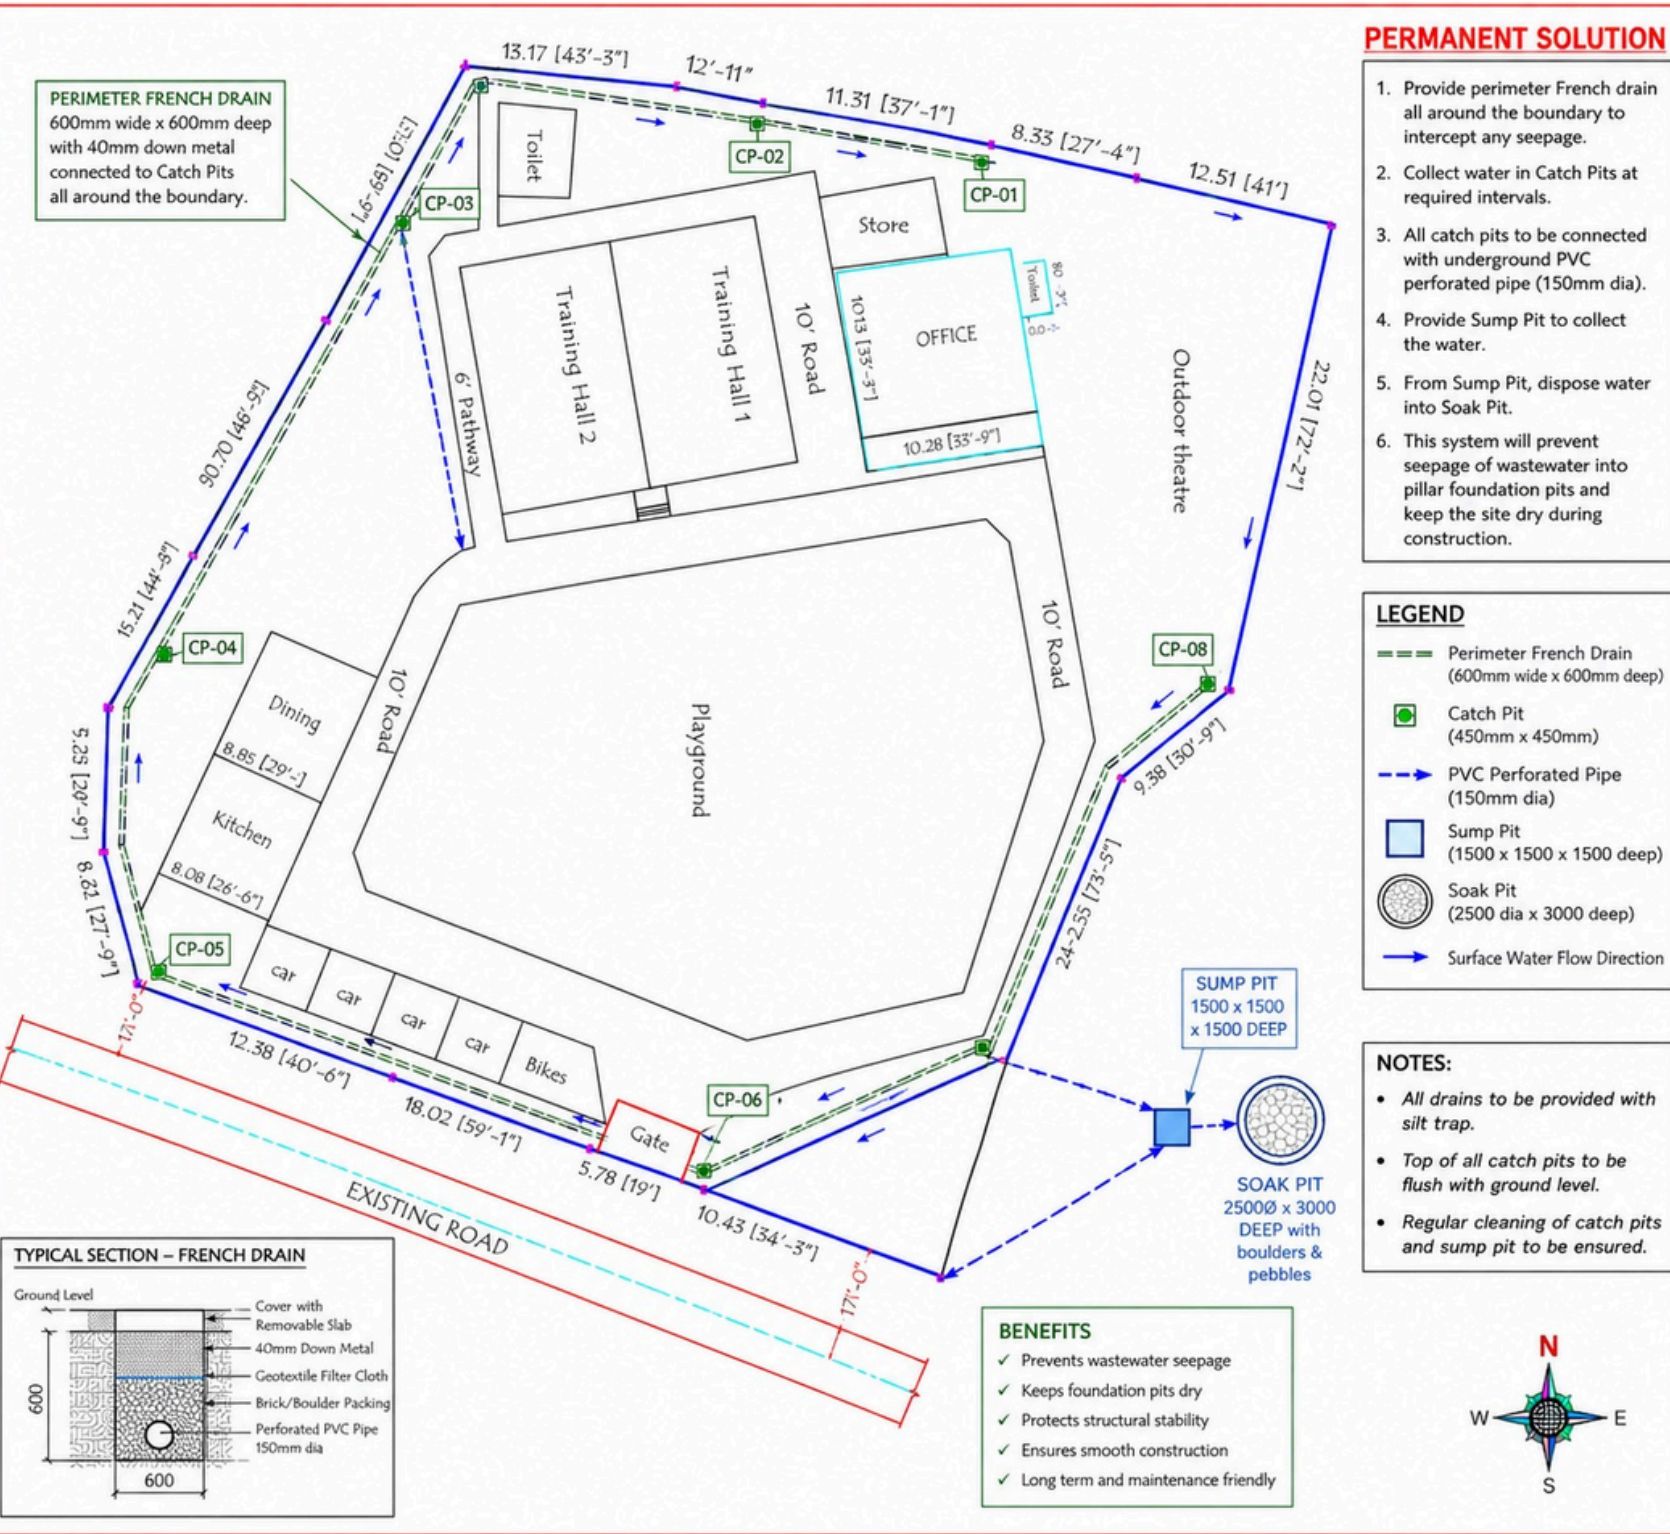

01/2026
01/2026
Secretary Veeravilli Agraharam.
Subject to this conditions
and down to this effect provided
G. Sankar in A.
Panchayat Secretary
Grama Panchayat
Veeravilli Agraharam
V. Madugula Mandalam

Unnathi Bhavan



Tezaswi Garu
& Family

Siri Foundation
& Team

Asha for Education

Spoorthi NGO

Our heartfelt thanks to our well-
wishers for their valuable support.



Srujanavani Voluntary Association

INVITES ALL WELL-WISHERS TO THE

BHOOMI PUJA

భూమిపూజ

OF THE

UNNATHI BHAVAN PROJECT



Join Us as We Lay the Foundation for a Brighter Future!

DATE 12th April 2026 (Sunday)

TIME 9 a.m.

VENUE Srujanavani Skill Development Centre,
Vaddadi, V-Madgula, Anapalli, A.P

Soil Excavation & Foundation Work



Soil Excavation & Foundation Work





Foundation Construction & Ground Beam Work





Building Superstructure – Columns & Brick Masonry







Generated by AI

For Kitchen & Dinning In Association with Octave Technologies, Hyderabad

Committed Amount - 28L

Released Amount - 10L

Milestone	Key Activity	Expected Output	Status
1	Statutory approvals & site planning	Received Panchayat approval, Struictural designs from authorized structrual engineer,	Completed
2	Final site layout, setting-out and level verification.	Approved site setting-out and benchmark levels.	Completed
3	Foundation, footing works, Plinth beam, columns, septic tank	Foundations completed and verified before RCC progression, RCC structural works: ooting works, Plinth beam, columns, septic tank	Completed
4	brick work, Slab as per approved structural drawings.	brick work and Structural frame completed for the planned phase.	Construction stage
5	Masonry, waterproofing, plumbing and electrical first-fix works.	Building envelope and service first-fix completed.	Yet to start
6	Flooring, doors/windows, painting, sanitary and electrical finishing, Buidling Elevation	Internal and external finishing complete	Yet to start
7	Final stage	Ready-for-use facility and completion records.	Expected to be completed By end of November 2026

Budget Balance Sheet

Category	Amount Spent
Unnathi Bhavan (Training Hall)	2345905
Kitchen & Dining	0
Library	0
Landscaping	0
Boundary Walls	665600
Total	3011505

Funds received from	Date	Amount
M/s SPOORTHY Foundation	17-04-2025	761055
M/s SPOORTHY Foundation	30-04-2026	754769
M/s Asha for Education	12-09-2025	800000
M/s Asha for Education	15-09-2025	850000
Srujanavani		2000000
Total	As on Aug 2026	5165824
Spent Amount	As on 10 Aug 2026	3011505
Balance Amount	As on 10 Aug 2026	2154319

Thank You

