



Asha
for Education

Bringing hope through education

VARUN Hostel Construction Update

February 15, 2024

Suhas Satheesh

suhas.satheesh@gmail.com

Location & Background

- Asha SV funding since 2003
- 11 centers across UP-Bihar border
- All schools are **informal centers** in isolated forest villages of 40-50 families
- Road access: Only 1 center - Shahpur
- Toilets, solar panels, first aid boxes, library, drinking water added in past 3 years
- Used to be naxal affected, not anymore; heavy CRPF presence in Naugarh



Leaders On Ground

- Dr. S. P. Singh
 - ◆ PhD in agriculture
 - ◆ Co-founder of VARUN
 - ◆ Spent all his life at VARUN
 - ◆ 60+ years old, few health issues

- Ram Krit
 - ◆ Right hand man for Dr. Singh
 - ◆ 37 years old, B.A. degree
 - ◆ Student of VARUN
 - ◆ Administrator for VARUN

- Ramesh
 - ◆ Long time VARUN employee
 - ◆ No education, but skilled



Dr. S. P. Singh

Ram Krit

Ramesh

Aurawatand



Jhariyawar




Bhaganda



Shahpur



सामुदायिक शिक्षा केन्द्र
काठमाडौं - विभिन्न प्रयोग केन्द्र, अभ्यास केन्द्र, प्रशिक्षण केन्द्र
असुरा केन्द्र, स्वयं प्रशिक्षण केन्द्र
प्रशिक्षण - आरक्षण, दूरस्थ, दलाली, उच्च
महाम - कानुनी सम्बन्धित पत्र मन्त्र
उपनिर्देशक सहायक (VARUM)
स्थान - गंगा नगर, नौगढ़ - चन्द्रोली

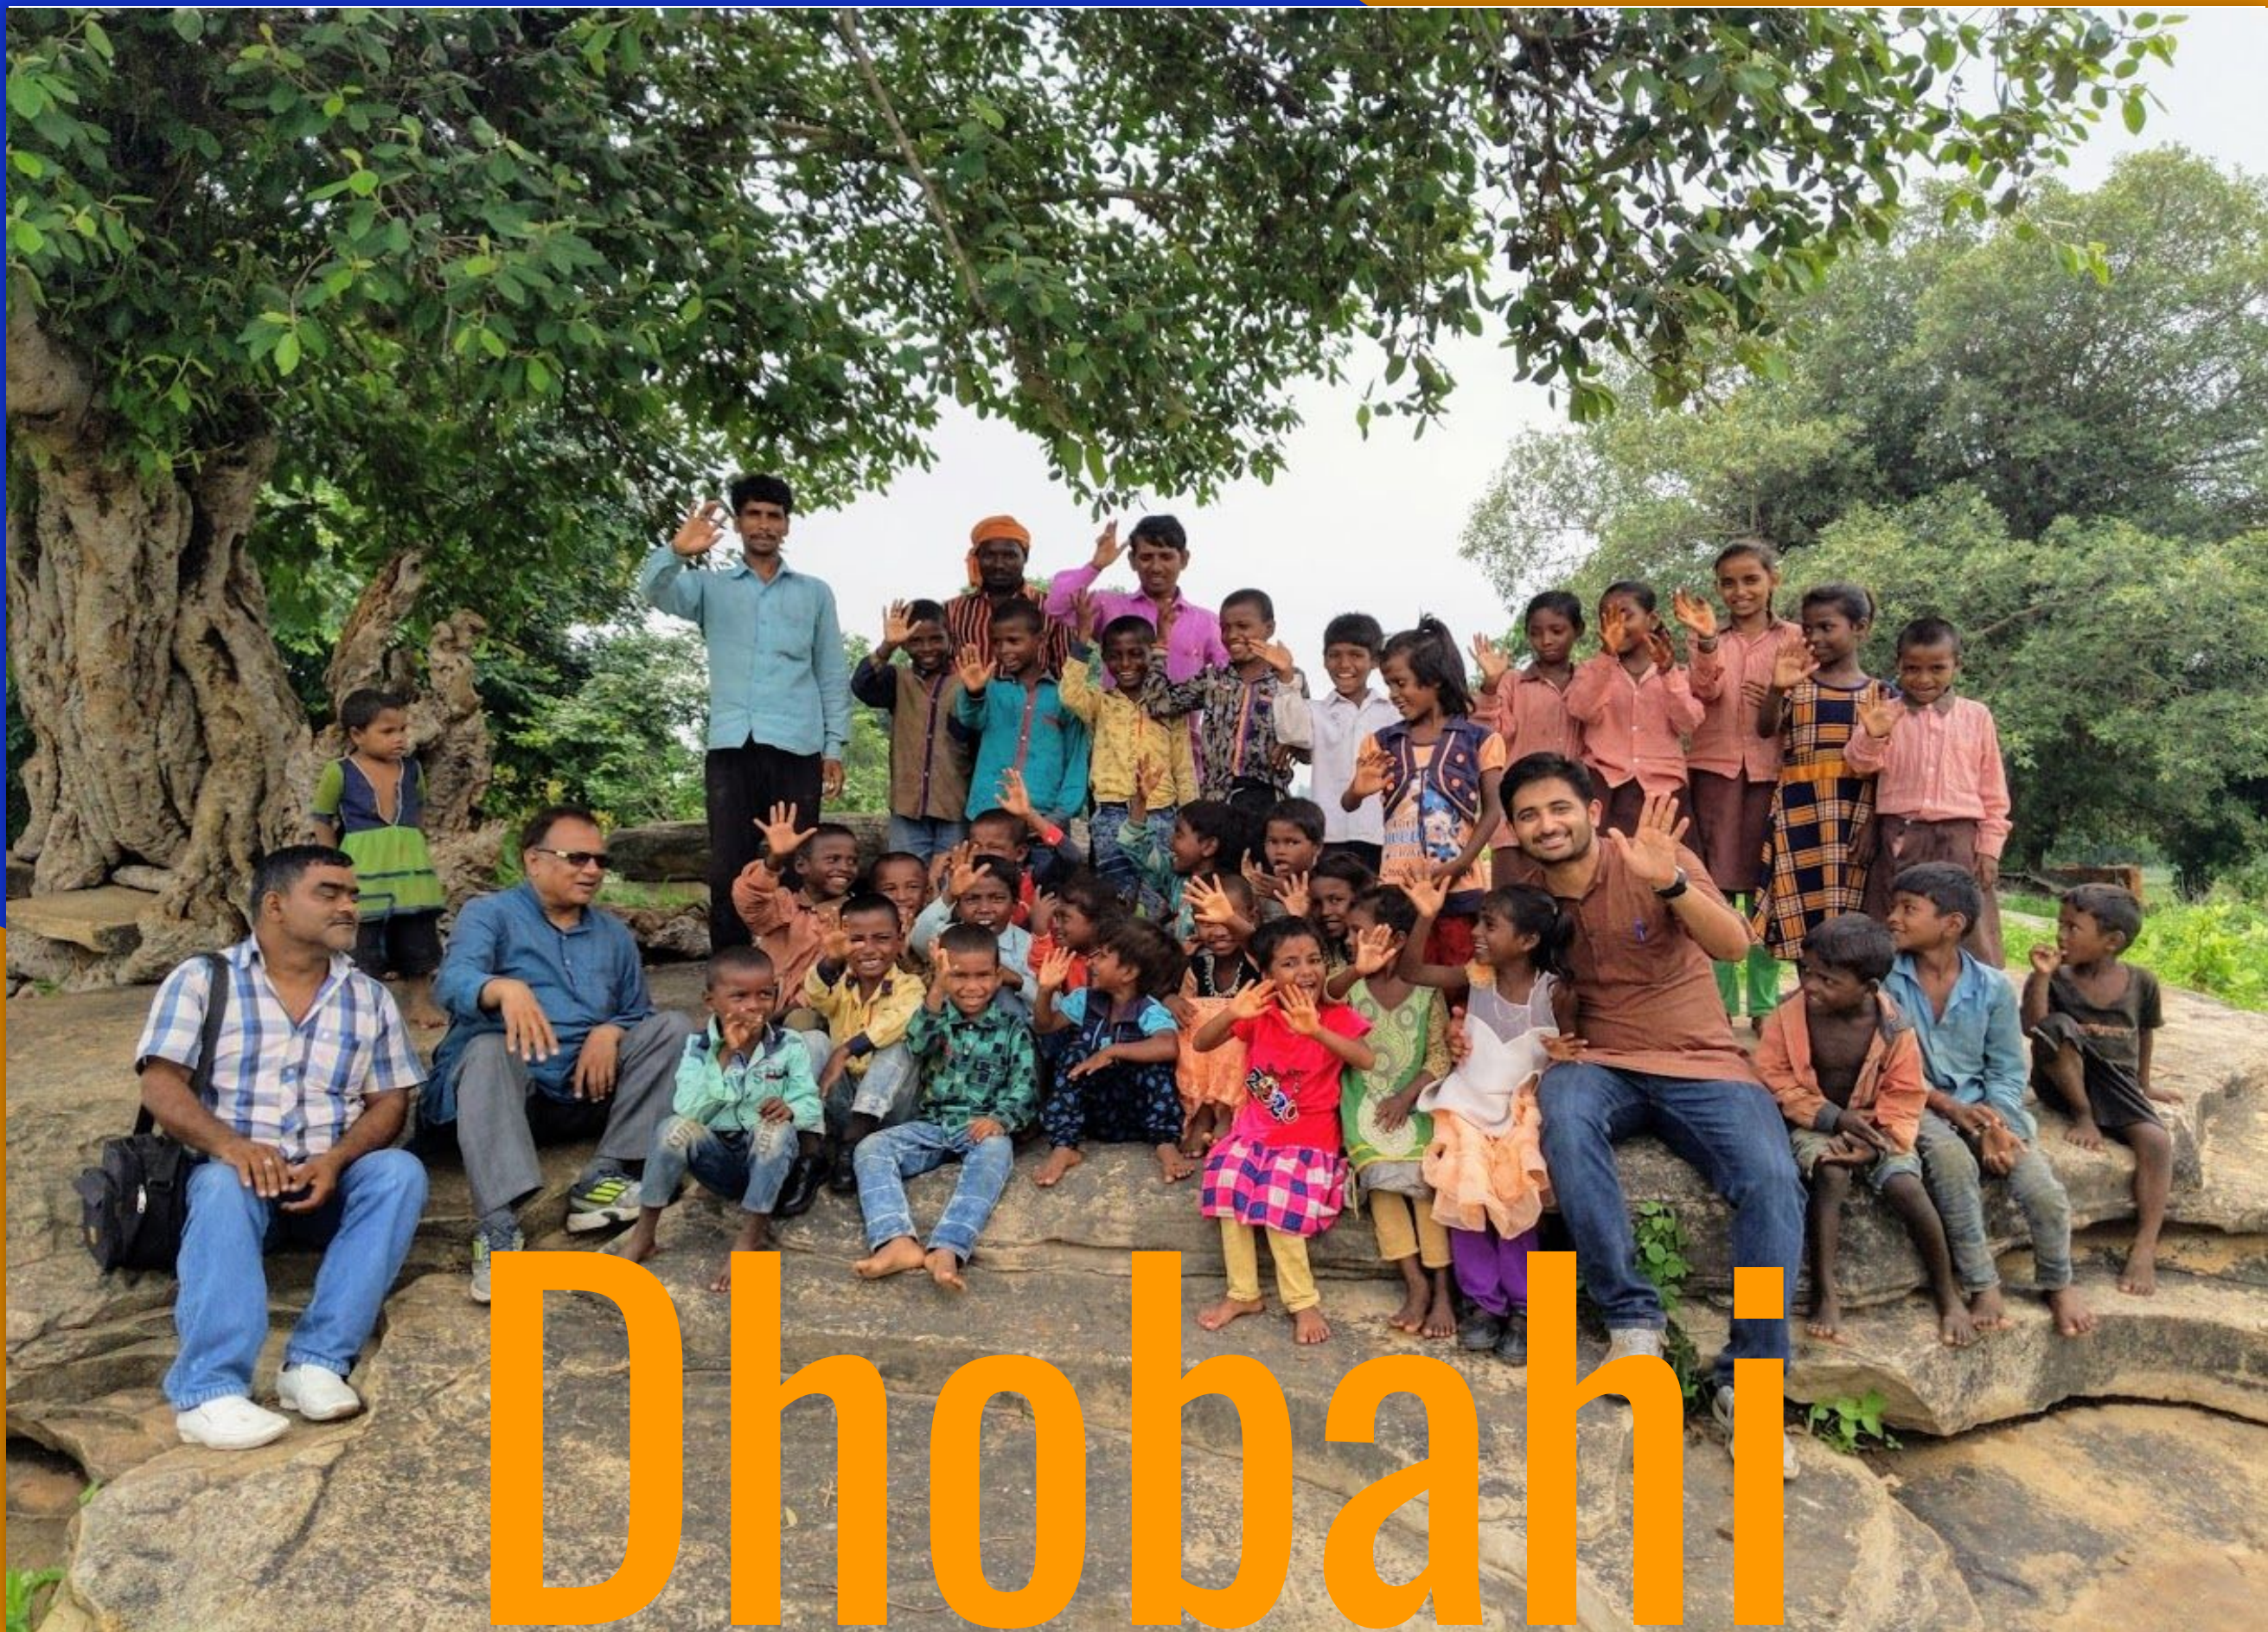

Dhobahi



सामुदायिक शिक्षा केन्द्र
CHILDREN ACTIVITIES CENTRE
ग्राम - नन्दना, नगवौ, सोनभद्र
प्रयोजक - आशा फार एडुकेशन
सहयोगी संस्था - बालुन्दरी एडुकेटेशन फार रूरल
अपलिफ्टमेंट सण्ड नेटवर्किंग (वरुन)

Nandana

Piranchua



Bhitari





Baluhriya

Nauvanar



GIRLS HOSTEL - Update

Numbers

Ist installment -

Received budget-Rs.16,30,000.00

S.N.	Particulars	Expences Amounts
01	Sand	1,38,868.00
02	Concrete	1,58,762.00
03	Cement	1,82,553.00
04	Ironrod & ring	5,96,963.00
05	Bricks	1,84,513
06	Celling molding	1,05,400
07	Electric pipe & plumber	12,745.00
08	Manson & labour charge	3,00,200.00
09	Miscelaneous	2,405.00
10	Total expences	16,82,409.00

Received budget- Rs. 16,30,000.00

Total Expences – Rs.16,82,409.00

Total over exps.- Rs.52,409.00

IInd installments-

Received budget-Rs.19,00,000.00

S.N.	Particulars	Expences Amounts
01	Sand	2,02,887.00
02	Concrete	1,32,516.00
03	Cement	2,35,037.00
04	Ironrod & ring	2,54,973.00
05	Bricks	2,43,000
06	Celling molding	1,13,305.00
07	Electric pipe & plumber	1,97,594.00
08	Manson & labour charge	3,43,600.00
09	Wood Materials	1,43,808.00
10	Door & Toilet Materials	61,110.00
11	Miscellaneous	870.00
-	Total Expences-	19,28,700.00

Received budget- Rs. 19,00,000.00

Total Expences – Rs.19,28,700.00

Total over exps.- Rs.28,700.00

Total Expenditure: 16,82,409+19,28,700=36,11,109.00

Excess spent = Rs.-81,109.00

Numbers

Expected needed amount

S.N.	Particulars	Expences Amounts
01	Sand	1,56,000.00
02	Concrete	35,000.00
03	Cement	1,20,000.00
04	Iron rod & ring	15,000.00
05	Bricks	1,00,000.00
06	Plumber	1,00,000.00
07	Electric materials & manson	3,00,000.00
08	Manson & labour charge	2,00,000.00
09	Wood Materials	50,000.00
10	Door & Toilet Materials	40,000.00
-	Total expected amounts-	11,16,000.00

Requesting a total of INR 12 lakhs to complete the hostel.

Part of this will come from Edu Impact 2022 budget and part from donor Anita.
